

**REHABILITATION OF CADANGAN MEMBINA  
DUA (2) BLOK PANGSAPURI KOS TINGGI (RP) 15  
TINGKAT (SEJUMLAH 360 UNIT) DENGAN 2  
TINGKAT PODIUM, 1 BLOK TEMPAT LETAK  
KERETA DAN 2 UNIT PENCAWANG ELEKTRIK  
SERTA KEMUDAHAN KOLAM RENANG DI ATAS  
SEBAHAGIAN TANAH KERAJAAN, OFF JALAN  
KUARI, CHERAS BARU, MUKIM AMPANG,  
DAERAH HULU LANGAT, SELANGOR DARUL  
EHSAN BAGI MUDI ANGKASA DEVELOPMENT  
SDN. BHD. (IN LIQUIDATION)**

## **Summary of work done as of 1 st half of October 2012:**

### **CAR PARK:**

- 1) Structure: All balanced parapet walls completed;
- 2) Brick work: All balanced brick work and coping completed;
- 3) Plastering:
  - a) Internal plastering – all completed from Level 2 to Level 5A;
  - b) External plastering – 90% completed for left elevation; 75% of the external scaffold for external wall plastering completed;
- 4) Electrical services: wiring checking from Level LG to Level 4 completed;

### **BLOCK A:**

- 1) Structure: Balanced roof beams, lift motor room and water tank level to complete;
- 2) Brickwork: Balanced 1 unit at Level 15, partition wall and lift motor room to complete;
- 3) Plastering:
  - a) Internal plastering – 3 units at Level 14 completed;
  - b) External plastering – first bay of external wall plastering started;
- 4) Electrical services:
  - a) Wiring checking for final sub circuit completed from Level 1 to Level 12;
  - b) Install sub main cable trunking at corridor completed from Level 1 to Level 10;
- 5) Plumbing works: checking, make good and pressure test for previous work done completed from Level 1 to Level 5

### **BLOCK B:**

- 1) Structure: Balanced water tank level to complete;
- 2) Brickwork: Balanced water tank level to complete;
- 3) Plastering:
  - a) Internal plastering – all completed except repairing works on work done by previous contractor;
  - b) External plastering – first bay of external wall plastering completed; second bay will start on 24 October 2012; plastering for staircase 4 started and target to complete on 25 October 2012;
- 4) Electrical services:
  - a) Wiring checking for final sub circuit completed from Level 1 to Level 14
  - b) TNB inspection for the TNB substation;
- 5) Plumbing works: checking, make good and pressure test for previous work done completed from Level 1 to Level 5;

CADANGAN MEMBINA & MENYIAPKAN KERJA-KERJA YANG TERBENGKALAI UNTUK NUSA MEWAH CONDO

PHYSICAL CPM S-CURVE

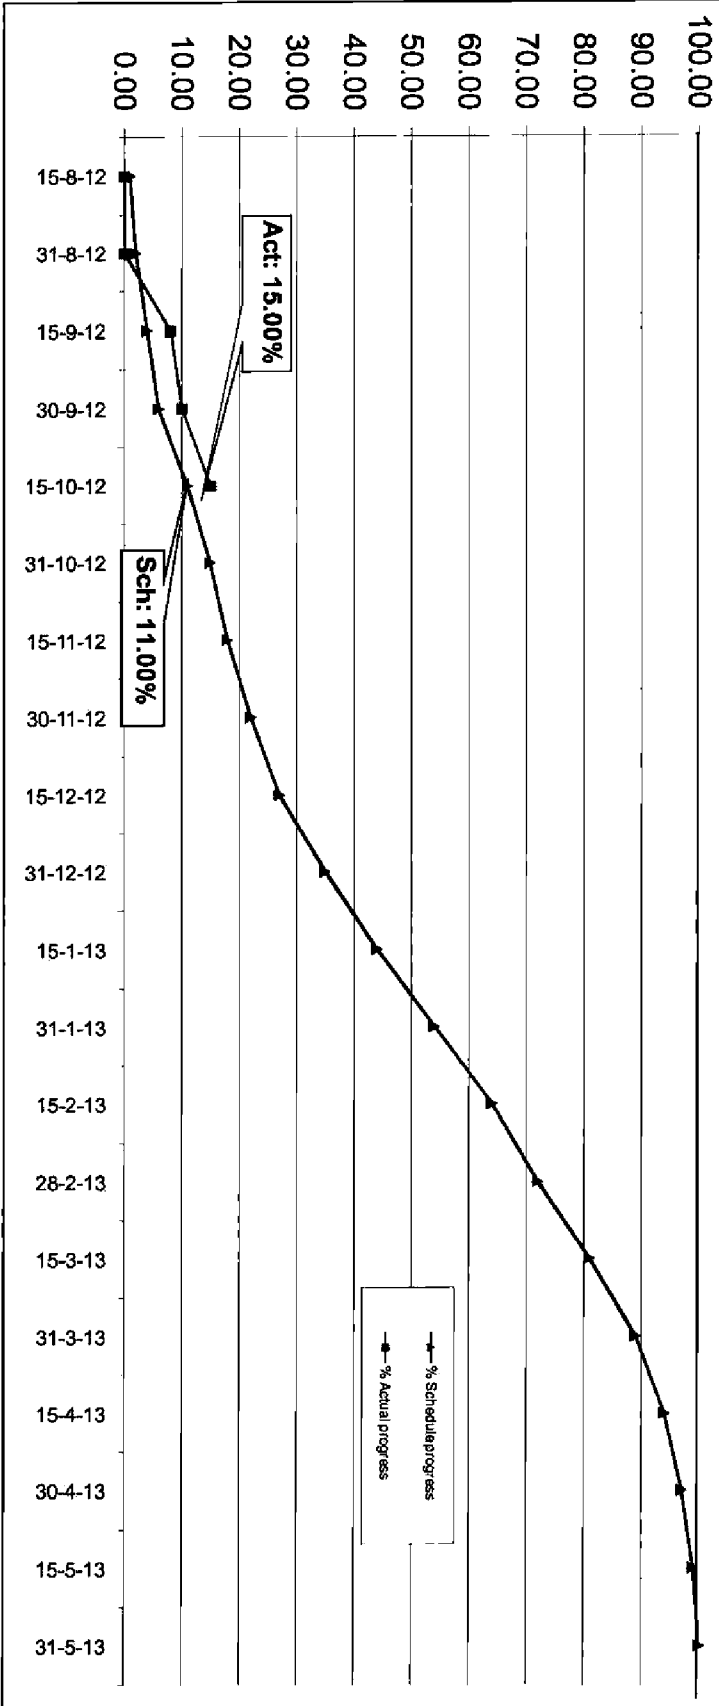


Chart 1

% Schedule progress	15-8-12	31-8-12	15-9-12	30-9-12	15-10-12	31-10-12	15-11-12	30-11-12	15-12-12	31-12-12	15-1-13	31-1-13	15-2-13	31-2-13	15-3-13	31-3-13	15-4-13	30-4-13	15-5-13	31-5-13
% Actual progress	0.00	0.00	0.00	8.00	10.00	15.00	18.00	22.00	27.00	35.00	44.00	54.00	64.00	72.00	81.00	89.00	94.00	97.00	99.00	100.00
